GEC, LLC

Mon 11/4/24

PEJ Stadium
Contract Completion Schedule

This schedule is contingent upon Pay Estimates being approved by the Eng, (DPW Commissioner)within 10 days as required by the contract.

ID	SOV #	Contract	Task Name	Duration	Start	Finish
20	B 18(iv) S	Sup	Doors Building Storage Areas	79 days	Thu 3/20/25	Tue 7/8/25
28	B 23(iii) S	Sup	Bull pen markings PEJ	30 days	Thu 3/20/25	Wed 4/30/25
79	E 6b(iii) S	Sup	Procure 8 Royal Palms Landscaping	65 days	Fri 3/21/25	Thu 6/19/25
78	E 6a(vi) S	Sup	Sidewalk from entry stairs to Main roadway to West	68 days	Sat 3/22/25	Tue 6/24/25
71	E 6(ii) S	Sup	Parking area between PEJ and TM field	60 days	Tue 3/25/25	Mon 6/16/25
30	B 25b O	Orig.	Installation (exhaust fans)	70 days	Wed 3/26/25	Tue 7/1/25
82	B 4(iig) A	a la carte	Add Backs on PEJ Bleachers	1 day	Tue 4/1/25	Tue 4/1/25
54	C 6(iii) S	Sup	Plumbing stubouts at walls TM	30 days	Thu 4/3/25	Wed 5/14/25
57	C 6(vi) S	Sup	Electrical in walls TM	30 days	Thu 4/3/25	Wed 5/14/25
61	C 9(ii) S	Sup	Interior framing and walls TM Restroom	30 days	Thu 4/3/25	Wed 5/14/25
64	C 9(v) S	Sup	Floor finishes TM Restroom	30 days	Thu 4/3/25	Wed 5/14/25
8	B 11(iii) S	Sup	Paint Concessions	64 days	Tue 4/8/25	Fri 7/4/25
16	B 17(iii) S	Sup	Paint Ticket & Gate Control	64 days	Tue 4/8/25	Fri 7/4/25
19	B 18(iii) S	Sup	Paint Building Storage Areas	64 days	Tue 4/8/25	Fri 7/4/25
29	B 23(iv) S	Sup	Backstop netting & Pads PEJ	30 days	Thu 4/17/25	Wed 5/28/25
68	E 4(iii) S	Sup	Wire installation Site	60 days	Mon 4/21/25	Fri 7/11/25
67	E 4(ii) S	Sup	Light Fixtures installation Site	59 days	Wed 4/23/25	Mon 7/14/25
48	C 4(iic)	Sup	Concrete materials treads/risers for bleacher seats TM	1 day	Fri 4/25/25	Fri 4/25/25
50	C 4(iif) S	Sup	Aluminum benches installation TM	79 days	Mon 4/28/25	Thu 8/14/25
55	C 6(iv) S	Sup	Plumbing fixtures TM	60 days	Thu 5/1/25	Wed 7/23/25
58	C 6(vii) S	Sup	Electrical fixtures TM	60 days	Thu 5/1/25	Wed 7/23/25
59	C 6(viii) S	Sup	Exhaust fans TM	60 days	Thu 5/1/25	Wed 7/23/25
62	C 9(iii) S	Sup	Paint TM Restroom	30 days	Wed 5/7/25	Tue 6/17/25
63	C 9(iv) S	Sup	Doors - toilet partitions TM Restroom	50 days	Tue 5/20/25	Mon 7/28/25
77	E 6a(v) S	Sup	Sidewalk from parking to TM field	30 days	Thu 5/22/25	Wed 7/2/25
76	E 6a(iv) S	Sup	Accessible ramp from parking to PEJ stadium	30 days	Mon 5/26/25	Fri 7/4/25
80	E 6b(ii) S	Sup	Install palms and landscaping	45 days	Mon 5/26/25	Fri 7/25/25
72	E 6(iii) S	Sup	Striping for Parking area	30 days	Thu 6/12/25	Wed 7/23/25
73	E 6(iv) S	Sup	Signage for Parking area	30 days	Thu 6/12/25	Wed 7/23/25
22	B 19d O	Orig.	Bat and helmet rack installation Dugouts	20 days	Fri 6/20/25	Thu 7/17/25
25	B 21a(iv) S	Sup	Field Markings	15 days	Fri 6/20/25	Thu 7/10/25
52	C 5(iii) S	Sup	Field Markings TM	11 days	Fri 6/20/25	Fri 7/4/25
102			Contract Closeout	31 days	Fri 6/27/25	Fri 8/8/25
1			Government Punch List	13 days	Fri 6/20/25	Tue 7/8/25

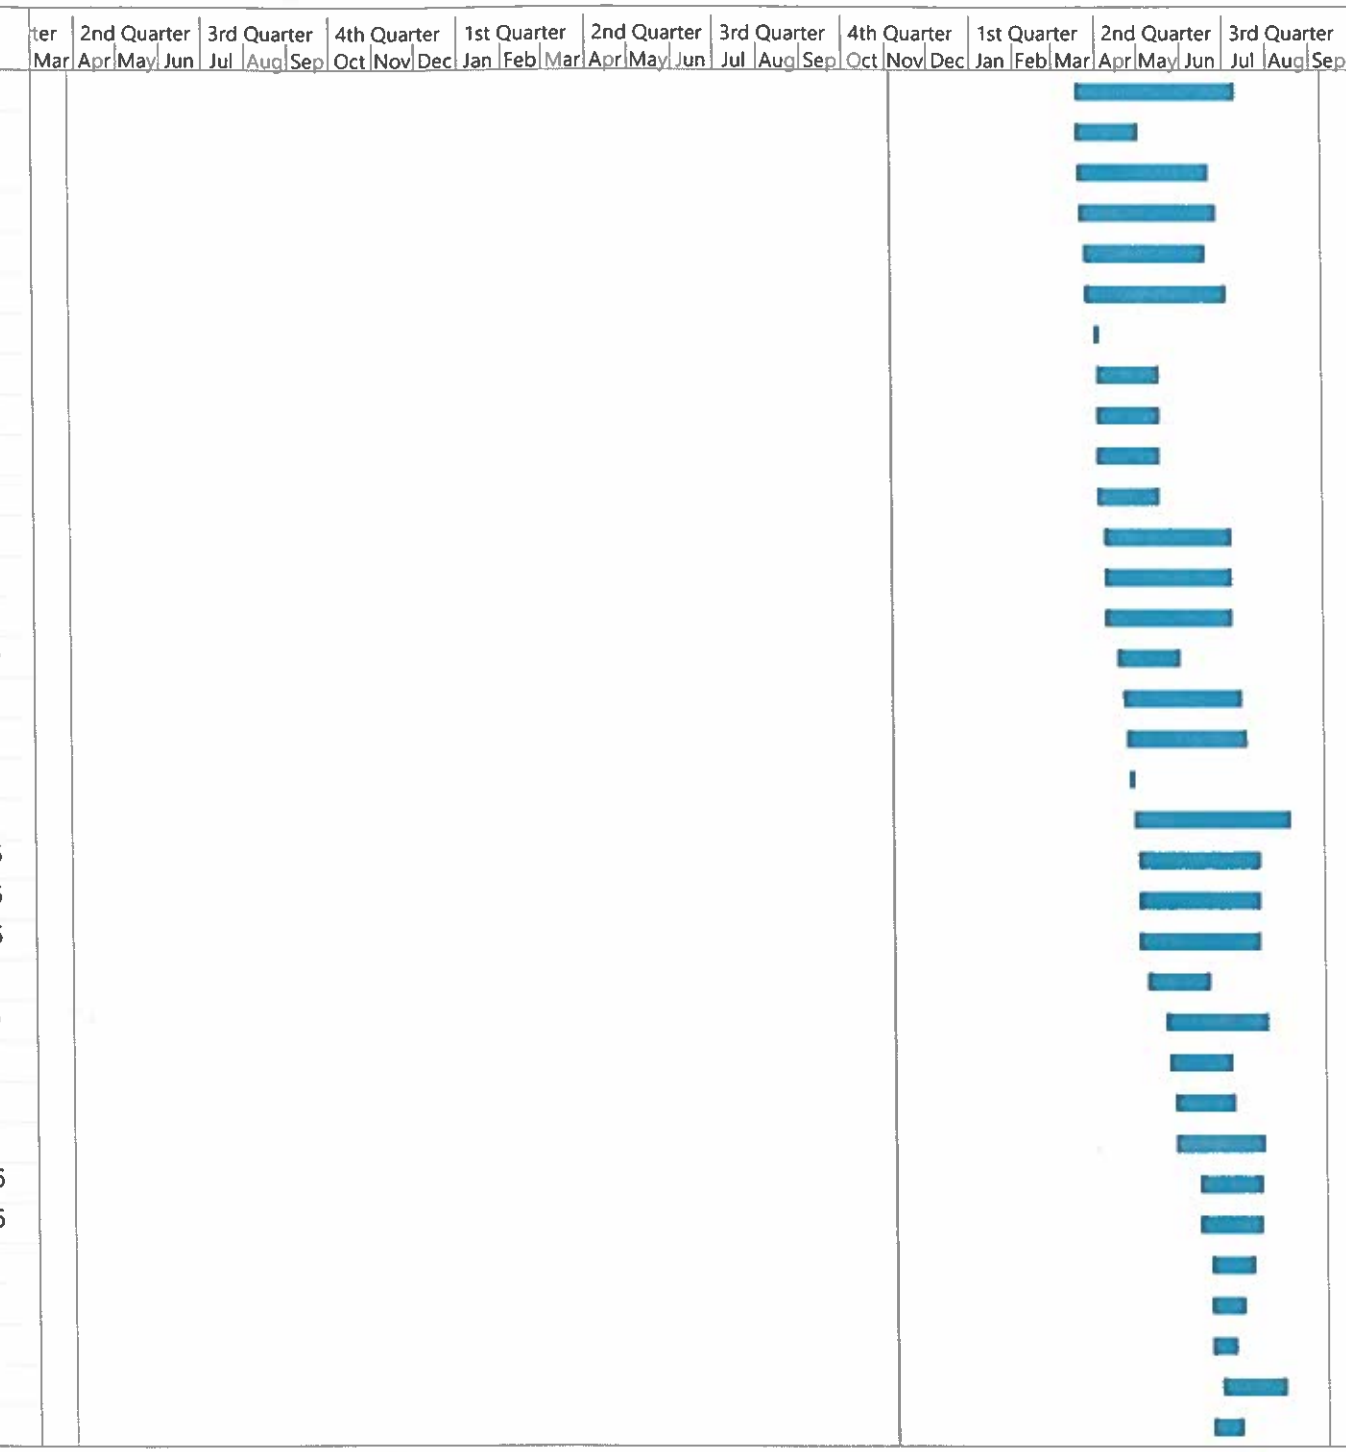

Project: PEJ Contract Co
Date: Mon 11/4/24

Task		Project Summary		Manual Task		Start-only		Deadline	
Split		Inactive Task		Duration-only		Finish-only		Progress	
Milestone		Inactive Milestone		Manual Summary Rollup		External Tasks		Manual Progress	
Summary		Inactive Summary		Manual Summary		External Milestone			
